

Tuesday, June 14, 2016 11:52:34 AM

145714

Page 1

Accept

N900040100

Setup Start *NS1*

Stop *NS2*

Item Name: Aft Post Mount Assembly 119 X tubes.

Start Date: 5/25/2016 **Start Qty:** 12.00 ***12***

Cust Item ID:

Required Date: 6/1/2016 **Req'd Qty:** 12.00 ***12***

Customer:

Reference:

Approvals: **Process Plan:** dm **Date:** 16/06/14

Tooling: _____ **Date:** _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D5152	B

110	Weld per dwg A/R S.S. rod Batch: <u>123823</u>	0.00
-----	--	------

110

Large Fab

Memo

Large Fab

120	QC9- Inspect visual per QSI004- Fusion Welds	0.00
-----	--	------

120

QC

Memo

Quality Control

130	QC5- Inspect part completeness to step on W/O	0.00
-----	---	------

130

QC

Memo

Quality Control

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Work Order ID 145714

Tuesday, June 14, 2016 11:52:34 AM

145714

Page 3

Item ID: D5152-043 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Aft Post Mount Assembly
Start Date: 5/25/2016 Start Qty: 12.00 ***12*** Cust Item ID:
Required Date: 6/1/2016 Req'd Qty: 12.00 ***12*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
170	QC21- Final Inspection - Work Order Release	0.00							
170									
QC	Memo	0.20							
Quality Control									

16/6/29 JF
Lm 16/06/29.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

Picklist Print

Tuesday, June 14, 2016 11:52:34 AM

Page 1

Work Order ID: 145714

145714

Parent Item: D5152-043

D5152-043

Parent Item Name: Aft Post Mount Assembly

Start Date: 5/25/2016

Required Date: 6/1/2016

Start Qty: 12.00

Required Qty: 12.00

Comments: IPP REV:A 15.01.09 NEW ISSUE DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D5152-3		Manufactured	No				Each	24.0000		12			
---------	--	--------------	----	--	--	--	------	---------	--	----	--	--	--

D5152-3

Aft Post Mount

16-06-21
JLM

Location

Loc Qty

Loc Code

WA002

24

142696

24

12

D5152-7		Manufactured	No				Each	18.0000		12			
---------	--	--------------	----	--	--	--	------	---------	--	----	--	--	--

D5152-7

Aft Step Post

16-06-21
JLM

Location

Loc Qty

Loc Code

WA002

18

143424

18

12

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

ITEM	QTY	P/N	DESCRIPTION
	X	D5152-041	FWD POST MOUNT ASSY
1	1	D5152-1	FWD POST MOUNT
2	1	D5152-5	FWD STEP POST

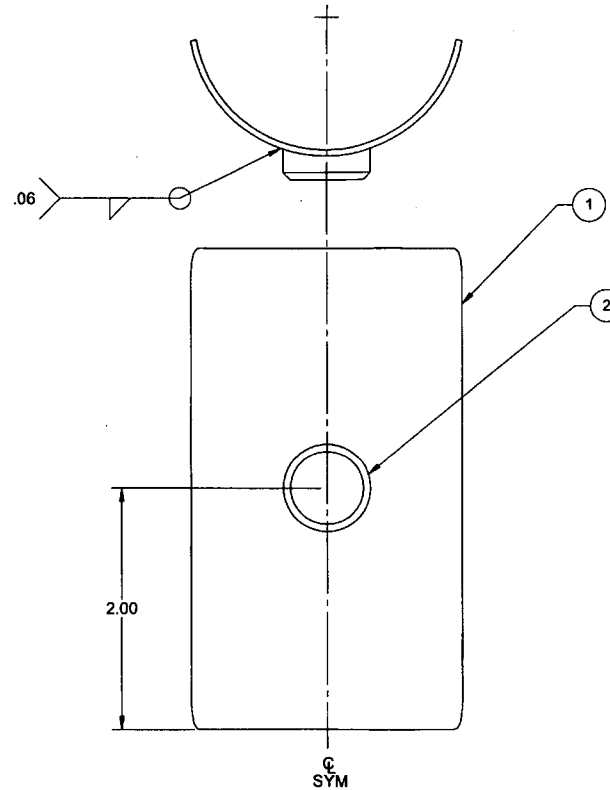

D5152-041 FWD POST MOUNT ASSEMBLY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: PRIME PER DART QSI 005 4.2
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
- 7) WEIGHT: D5152-041= 0.21 lbs

RELEASED

2015 FEB 09

ECN 15-516 9


B	COMPLETE REDESIGN, SEE PREVIOUS REV FOR DETAILS	DB	15.01.09
A	NEW ISSUE	DB	14.08.03
REV.	DESCRIPTION	BY	DATE
DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 1 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

APPROVED

w/p 145714

dm 16/06/14

ITEM	QTY -043	P/N	DESCRIPTION
	X	D5152-043	AFT POST MOUNT ASSY
1	1	D5152-3	AFT POST MOUNT
2	1	D5152-7	AFT STEP POST

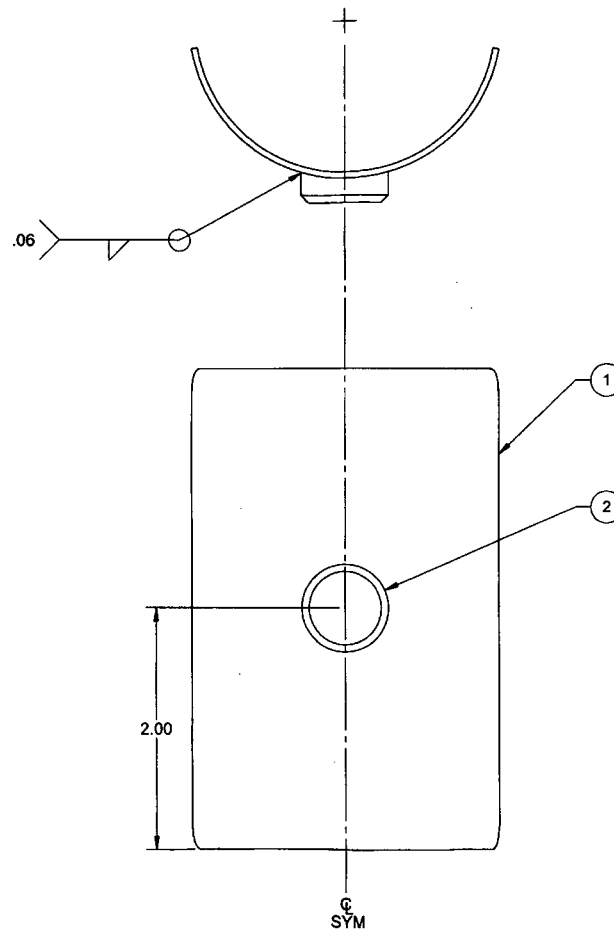

D5152-043 AFT POST MOUNT ASSEMBLY

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: PRIME PER DART QSI 005 4.2
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
- 7) WEIGHT: D5152-043= 0.23 lbs

RELEASED


2015 FEB 09

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO. D5152	REV. B
MFG. APPR.	DD		SHEET 2 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

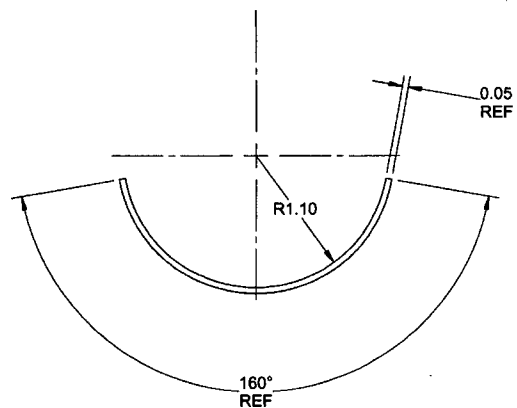

D5152-1 FWD POST MOUNT
(MAKE FROM D5152-1F)

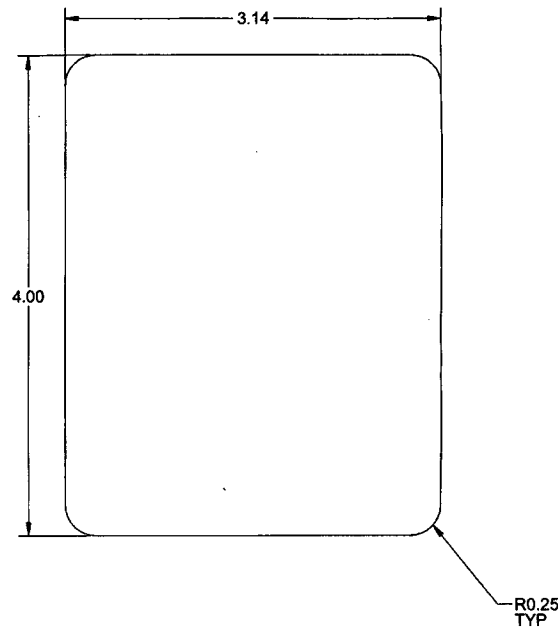

D5152-1F FWD POST MOUNT
(FLAT PATTERN)

RELEASED


2015 FEB 09

NOTES:


- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 3 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

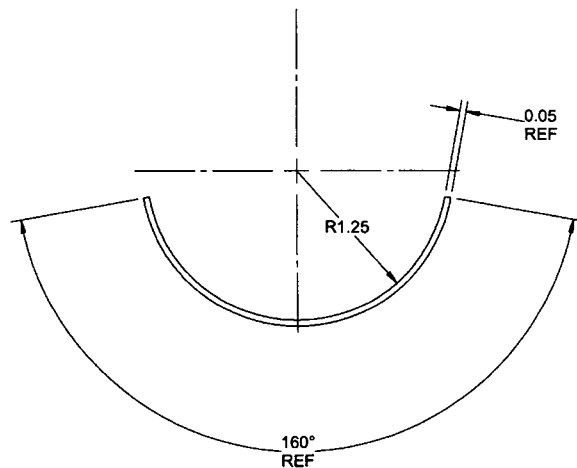

D5152-3 AFT POST MOUNT
(MAKE FROM D5152-3F)

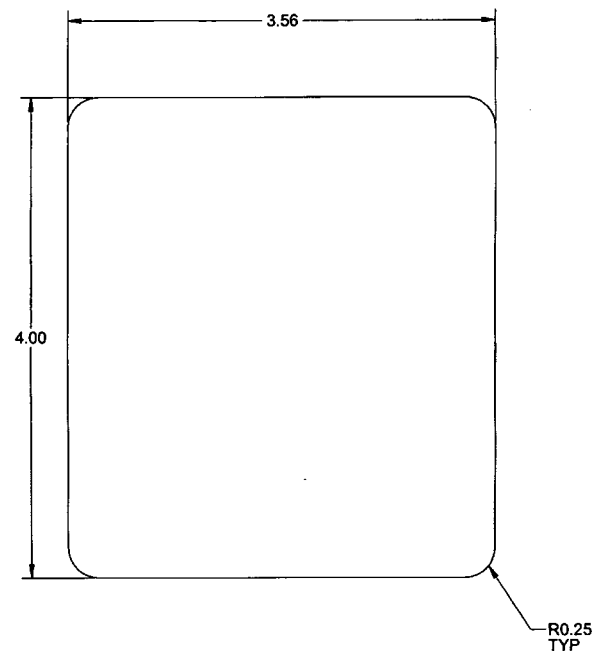

D5152-3F AFT POST MOUNT
(FLAT PATTERN)

RELEASED

2015 FEB 09

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	EPDMA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 4 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR LOANED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8

7

6

5

4

3

2

1

R1.150

0.20

0.06 X 45° CMF

Ø0.725

D5152-5 FWD STEP POST

R1.300

0.20

0.06 X 45° CMF

Ø0.725

D5152-7 AFT STEP POST**RELEASED**

2015 FEB 09

NOTES:

- 1) MATERIAL: AISI 304/316 SS ROUND BAR PER ASTM A276, REF DART SPEC M304R0.750
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.02 lbs

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 5 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8

7

6

5

4

3

2

1
